



AIIMS RAIPUR

PROJECT DETAILS


- ❖ **Location** : **NH-6 , GE Road, Tatibandh, Raipur**
- ❖ **Lat-Long** : **21°15'23.3" N, 81°34'44.9" E**
- ❖ **Railway Station** : **Raipur Junction (7.5 Kms)**
- ❖ **Airport** : **Raipur Airport (22.5 Kms)**
- ❖ **Total Land Area** : **63.85 Acres - Hospital & College Complex**
39.78 Acres - Residential Complex
103.63 Acres (Total)
- ❖ **Total Built-up Area** : **1,77,881 Sqmt.**
(Hospital & College Complex)
- ❖ **Total Built-up Area** : **15,256 Sqmt. (Residential Complex)**
- ❖ **Total Capital Cost** : **Rs. 840 Crores**




AIIMS RAIPUR

Overhead Water Tank

2,58,406 Sqm- (63.85 Acres)

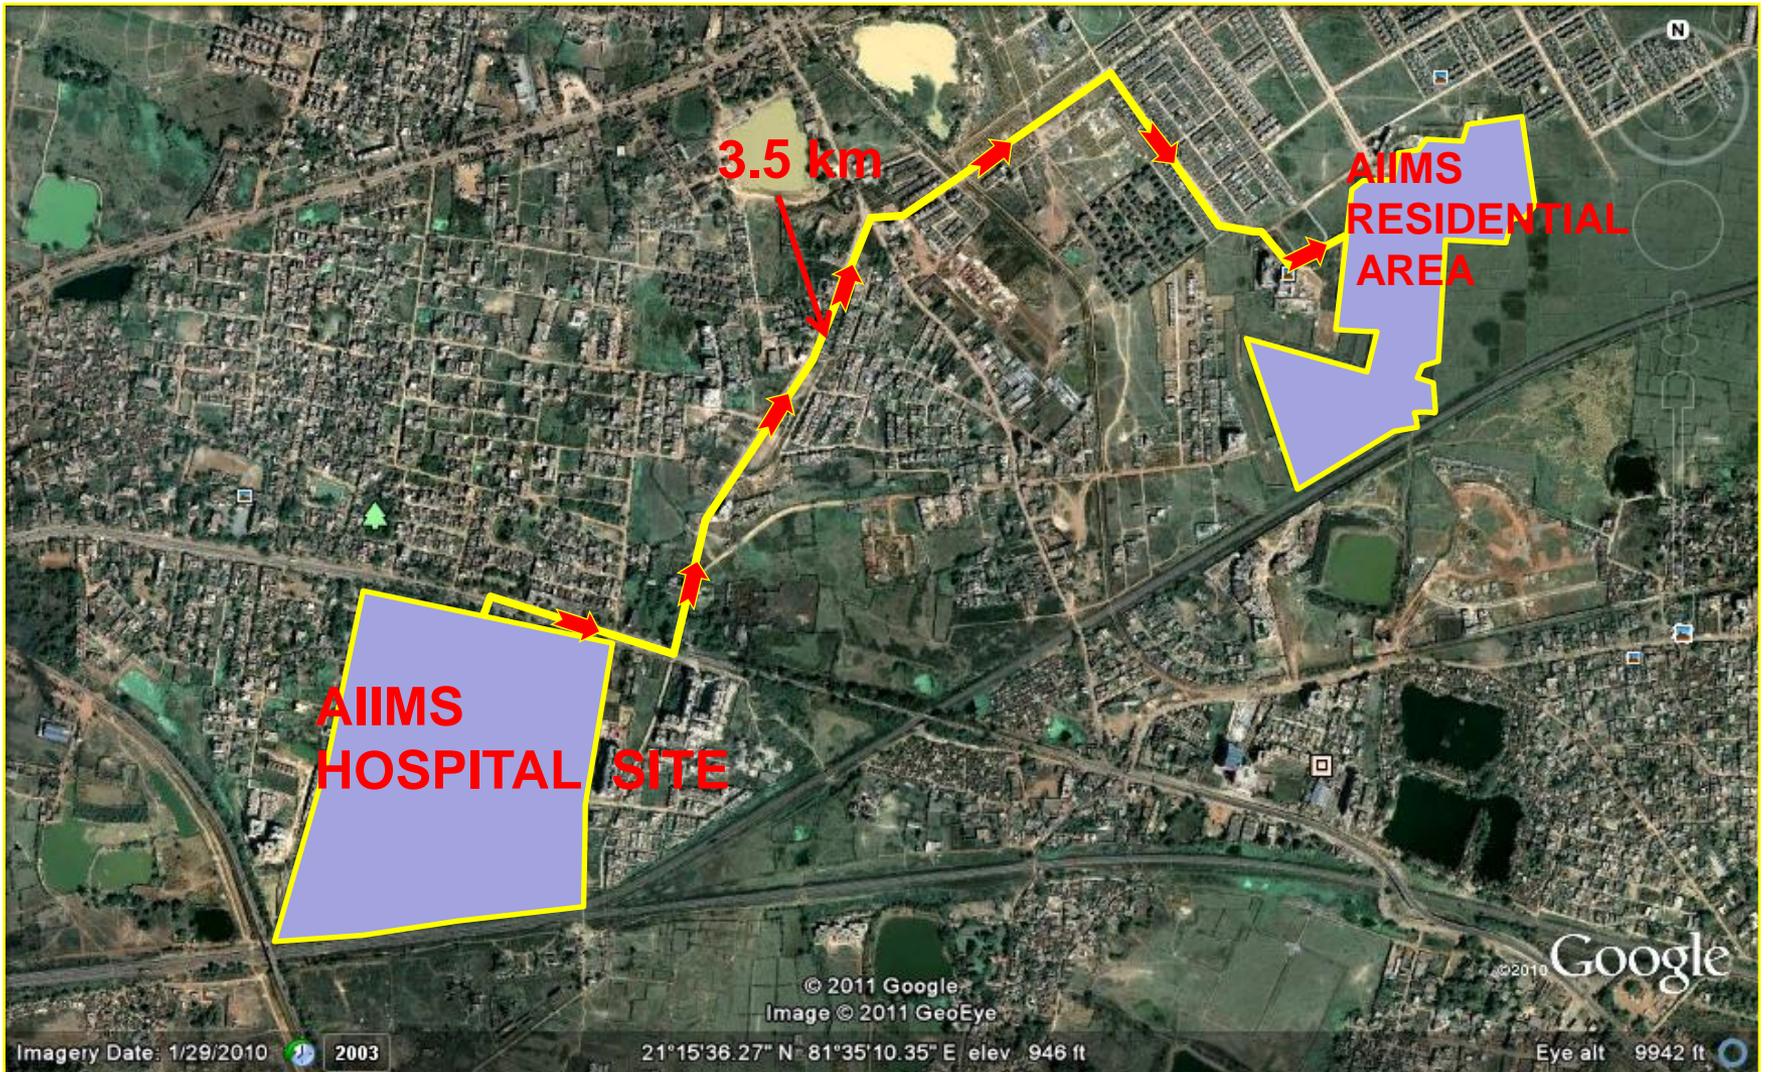

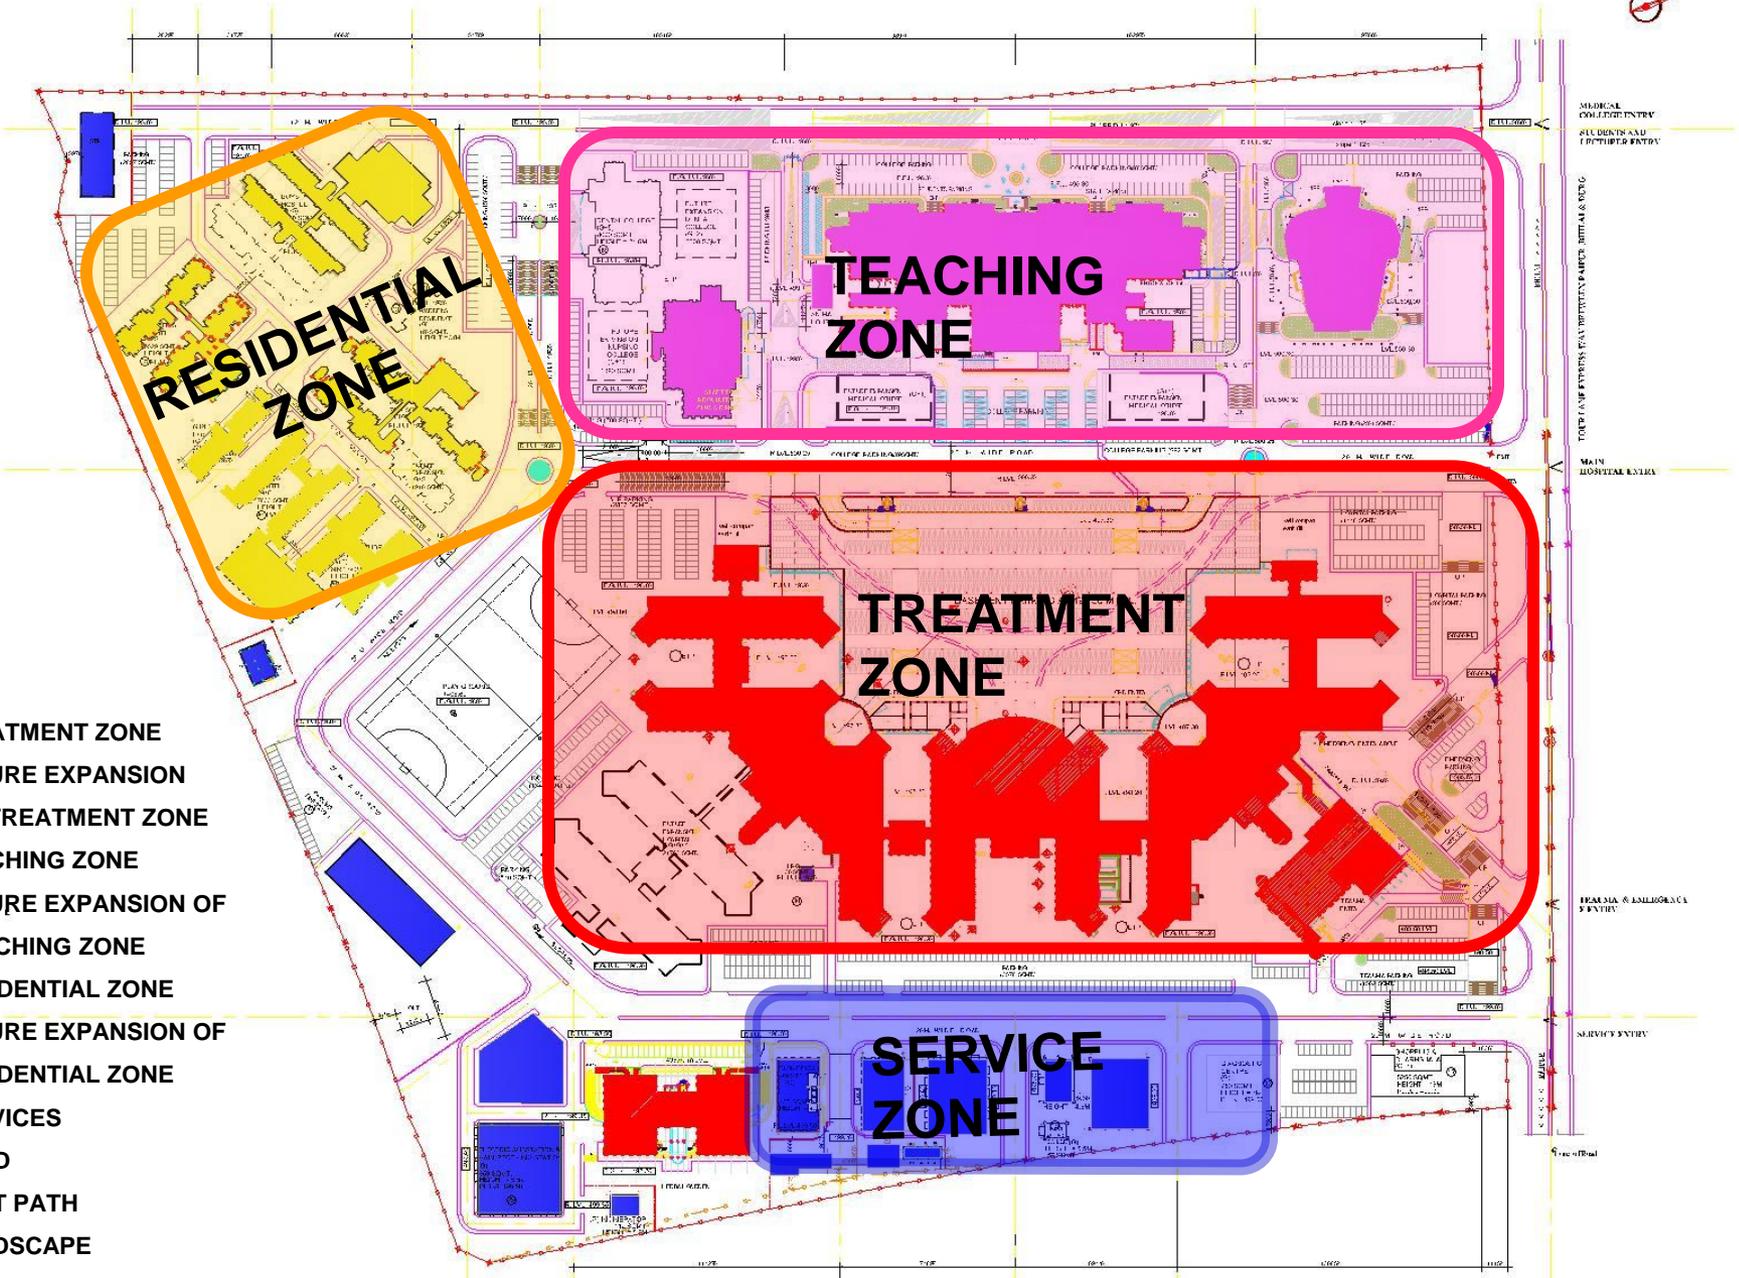

-  TREATMENT ZONE
-  FUTURE EXPANSION OF TREATMENT ZONE
-  TEACHING ZONE
-  FUTURE EXPANSION OF TEACHING ZONE
-  RESIDENTIAL ZONE
-  FUTURE EXPANSION OF RESIDENTIAL ZONE
-  SERVICES
-  ROAD
-  FOOT PATH
-  HARDSCAPE
-  PARKING
-  SOFTSCAPE

ZONING PLAN

SURGICAL COLLECTOR ENTRY
 STUDENTS AND VISITORS ENTRY
 TOUR CAMP EXPRESS (FUTURE) PARKING, BIPOLE & BICYCLE
 MAIN HOSPITAL ENTRY
 REAR MAIN & BALLROOM & ENTRY
 SERVICE ENTRY



MEDICAL COLLEGE



MEDICAL COLLEGE (ANOTHER VIEW)



MEDICAL COLLEGE, PORCH



MEDICAL COLLEGE, LOBBY (Ground Floor)



LECTURE THEATRE – II



Corridor in Medical College



CENTRAL LIBRARY (GF)



CENTRAL LIBRARY (GF)



CENTRAL LIBRARY (e-library at Third Floor)



Laboratory



Laboratory



Board Room



NURSING COLLEGE



NURSING COLLEGE – LECTURE THEATRE



NURSES STUDENTS' HOSTEL



BOYS' HOSTEL (Front View)



RESIDENTS' HOSTEL



TRAUMA CENTRE (NORTH SIDE)



TRAUMA CENTRE (Another view at night)



Kitchen & Cafeteria - TRAUMA CENTRE



Corridor at Ground Floor - TRAUMA CENTRE



OPD Reception - TRAUMA CENTRE



OPD at Ground Floor - TRAUMA CENTRE



IPD at First Floor - TRAUMA CENTRE



IPD at Second Floor - TRAUMA CENTRE



Diagnostic Lab in Trauma Centre



Diagnostic Lab in Trauma Centre



Operation Theatre at Trauma Block



PMR & AYUSH



Audiometry Room



ENT OPD ROOM



X-RAY ROOM



BRICK WORK NEARING COMPLETION (Hospital Building)



HOSPITAL 'A' BLOCK



HOSPITAL 'B' BLOCK OUTER PAINTING IN PROGRESS



33KV & 11 KV VCB Panels



DG Sets Remote Radiators & Chimney



Service Building Road & Parking for Trauma Block



Service Building Road & Parking for Trauma Block



Medical College Road



Medical College - Landscaping

REVIEW OF ERC ACHIEVEMENTS

REVIEW OF ERC ACHIEVEMENTS

On constitution of Empowered Review Committee at AIIMS Raipur vide MoH & FW letter No. Z-28016/11/2012-SSH dated 20th May 2013, regular meetings are being held at site, to review all the issues related to the Project.

(a) No. of ERC meetings held so far

Total Eleven meetings have taken place.

- (i) 04.06.13,
- (ii) 14.06.13,
- (iii) 02.07.13,
- (iv) 23.07.13,
- (v) 12.08.13,
- (vi) 25.09.13,
- (vii) 11.10.13,
- (viii) 29.10.13,
- (ix) 12.11.13,
- (x) 31.12.13 and
- (xi) 24.02.14.

(b) Nos. of Variation Cases cleared with details of financial implications:

Refer Table (70 cases – Rs. 13.63 Cr)

REVIEW OF ERC ACHIEVEMENTS

| Sl. No. | Deviation / Variation Cases | Nos of Cases cleared | Financial Effect (in Cr) | Remarks |
|---------|-----------------------------|----------------------|--------------------------|---------|
|---------|-----------------------------|----------------------|--------------------------|---------|

Package I : Construction of Medical College & Hostel Complex at AIIMS Raipur

| | | | | |
|----|---------------------------------------|-----------|-------------|--|
| 1. | Deviation Cases approved by ERC | Nil | - | |
| 2. | Substituted Item Cases cleared by ERC | 19 | 1.97 | |
| 3. | Extra Item Cases cleared by ERC | 03 | 0.39 | |
| | Total | 22 | 2.36 | |

Package II : Construction of Hospital Complex at AIIMS Raipur

| | | | | |
|----|---------------------------------------|-----------|-------------|--|
| 1. | Deviation Cases approved by ERC | 08 | 3.47 | |
| 2. | Substituted Item Cases cleared by ERC | 15 | 1.00 | |
| 3. | Extra Item Cases cleared by ERC | - | - | |
| | Total | 23 | 4.47 | |

REVIEW OF ERC ACHIEVEMENTS

| Sl. No. | Deviation / Variation Cases | Nos of Cases cleared | Financial Effect (in Cr) | Remarks |
|---|---------------------------------------|----------------------|--------------------------|---------|
| <u>Package III</u> : Electrical Services at AIIMS Raipur | | | | |
| 1. | Deviation Cases approved by ERC | 08 | 1.36 | |
| 2. | Substituted Item Cases cleared by ERC | - | - | |
| 3. | Extra Item Cases cleared by ERC | - | - | |
| | Total | 08 | 1.36 | |
| <u>Package IV</u> : Estate Services at AIIMS Raipur | | | | |
| 1. | Deviation Cases approved by ERC | 03 | 4.19 | |
| 2. | Substituted Item Cases cleared by ERC | 03 | (-) 0.08 | |
| 3. | Extra Item Cases cleared by ERC | 11 | 1.33 | |
| | Total | 17 | 5.44 | |
| | Grand Total | 70 | (+) 13.63 | |

HOUSING COMPLEX (Phase - I)

| | | |
|------------------------|----------|---|
| Contractor | : | M/s IVRCL Infrastructures & Projects Limited. |
| Contract Amount | : | Rs. 30.39 Crore |
| Start Date | : | 18th Sep 2008/ 06th Nov 2008 |
| Completion Date | : | 28th Feb 2010 |
| | : | Jul 2012 (Substation work) |

HOUSING COMPLEX (Phase – II)

- ❖ **HSCC Ltd. has been nominated to undertake Housing Project (Phase – II) for 177 Units for Rs. 100 Crore.**
- ❖ **Agreement finalized.**

Salient features of the AIIMS Housing Complex at Raipur

| Type | No. of Storey | No. of units | No. of Blocks | Area (sqm) |
|-------------------|---------------|--------------|---------------|------------|
| Type - I | G+3 | 36 | 02 | 1861.20 |
| Type - II | G+5 | 72 | 02 | 4585.80 |
| Type - III | G+5 | 18 | 01 | 1463.88 |
| Type - IV | G+7 | 21 | 01 | 2206.17 |
| Type - V | G+7 | 24 | 01 | 4188.08 |
| Director Bungalow | G+1 | 01 | 01 | 301.06 |
| Guest House | G+2 | 01 | 01 | 649.81 |

Total No. of Units = 171
Total No. of Blocks= 09.
STP= 01 No (400 cum capacity)
Substation= 01
UG Tank=01 No (Total cap-200KL)
DG sets=02 Nos of 200KVA.

Total Area of Construction = 15256 Sqm.





TYPE - V



TYPE - III



TYPE - IV



TYPE - II



TYPE - I (A)



TYPE - I (B)





Foundation stone laying of SPH

Inauguration of AIIMS Raipur
on 27th Feb' 2014



ALL INDIA INSTITUTE OF MEDICAL SCIENCES, RAIPUR CHHATTISGARH



MBBS 2012 batch

ALL INDIA INSTITUTE OF MEDICAL SCIENCES, RAIPUR CHHATTISGARH



MBBS 2013 batch

ALL INDIA INSTITUTE OF MEDICAL SCIENCES, RAIPUR CHHATTISGARH



B.Sc. (Hons) Nursing 2013 batch



CME on Road Traffic Accidents



CME on Polytrauma Management



Visit of Nobel Laureate
Prof. Robert Huber



Visit of the
Director,
AIIMS-Raipur,
to CRPF camp
at Ambikapur,
Chhattisgarh



Annual Day Function



Annual Day Function

OUT PATIENT CENSUS, AIIMS Raipur

OPD (Out Patient Department)

- OPD started functioning since **05.06.2013** in Medical College. Later on, it has been shifted to Trauma Block, since **Nov' 2013**.
- Since, Jun' 13, the total Out Patient Census tabulated month-wise as under :-

| 2013 | | | | | | | 2014 | | | |
|------------|------------|------------|------------|------------|------------|------------|------------|------------|------------|--------------|
| <i>Jun</i> | <i>Jul</i> | <i>Aug</i> | <i>Sep</i> | <i>Oct</i> | <i>Nov</i> | <i>Dec</i> | <i>Jan</i> | <i>Feb</i> | <i>Mar</i> | <i>Total</i> |
| 2279 | 3302 | 3034 | 3790 | 3848 | 4202 | 6661 | 10096 | 9877 | 12717 | 59806 |

Telemedicine:

- Telemedicine started since **04.04.2013** on every Mondays and Thursdays of the week. Till date 2321 patients of 22 Battalions of CRPF have been given medical assistance.
